


## Physical Progress as of 31 March 2018

S.No	Item of work	Lining (km)		Achievement	Structures (nos.)		Achievement
		Estimate	Achievement	%	Estimate	Achievement	%
1	Left Bank Canal	14.74	14.20	96	74	74	100
2	Right Bank Canal	74.24	52.85	71	392	350	89
3	Distributary	26.10	26.10	100	212	212	100

### PHYSICAL PROGRESS:LINING

■ Lining (km) Estimate   
 ■ Lining (km) Achievement   
 ■ Achievement %

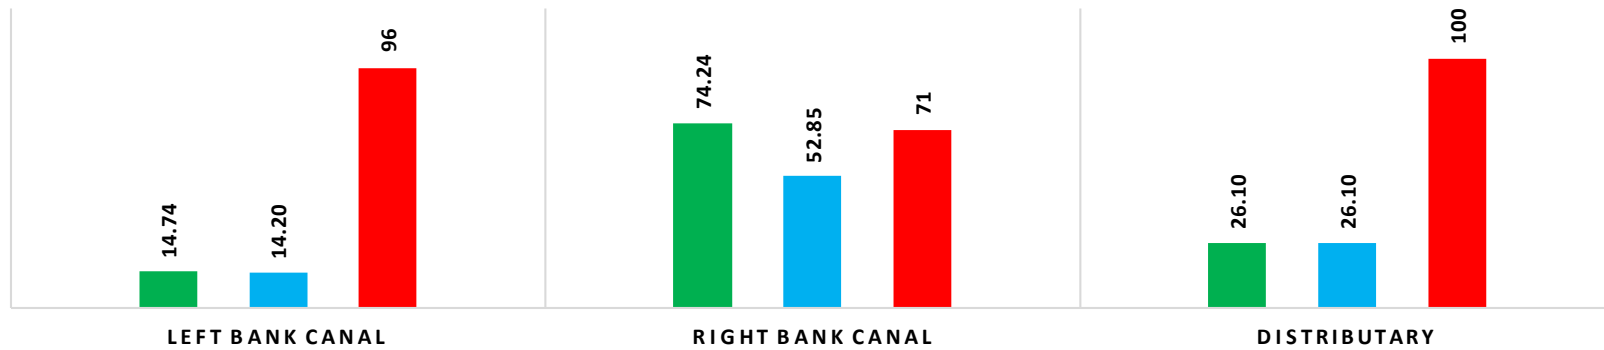

### PHYSICAL PROGRESS:STRUCTURES

■ Structures (nos.) Estimate   
 ■ Structures (nos.) Achievement   
 ■ Achievement %

