



Gondi Main works: Physical Progress as of 30 December 2019

S.No	Item of work	Lining (km)		Achieved	Structures (nos.)		Achieved
		Estimate	Achieved	%	Estimate	Achieved	%
1	Left Bank Canal	14.74	14.20	100.00	74	81	109.46
2	Right Bank Canal	74.24	72.21	97.27	392	385	98.21
3	Distributary	26.10	26.10	100.00	212	212	100.00

Physical Progress: Lining

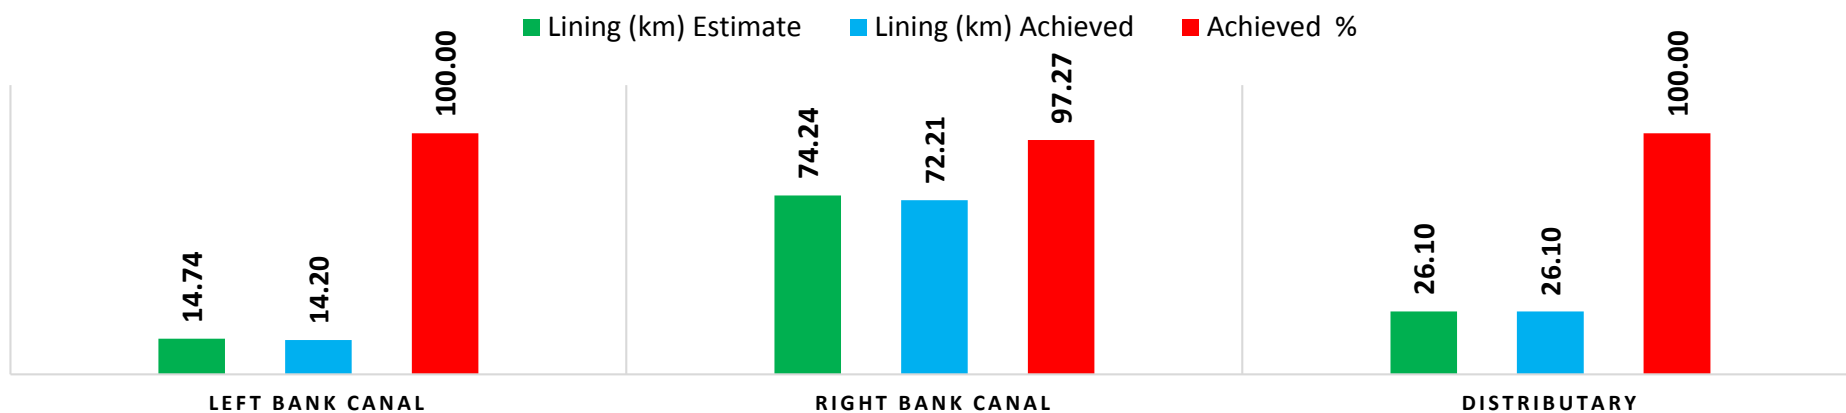


Physical Progress: Structures

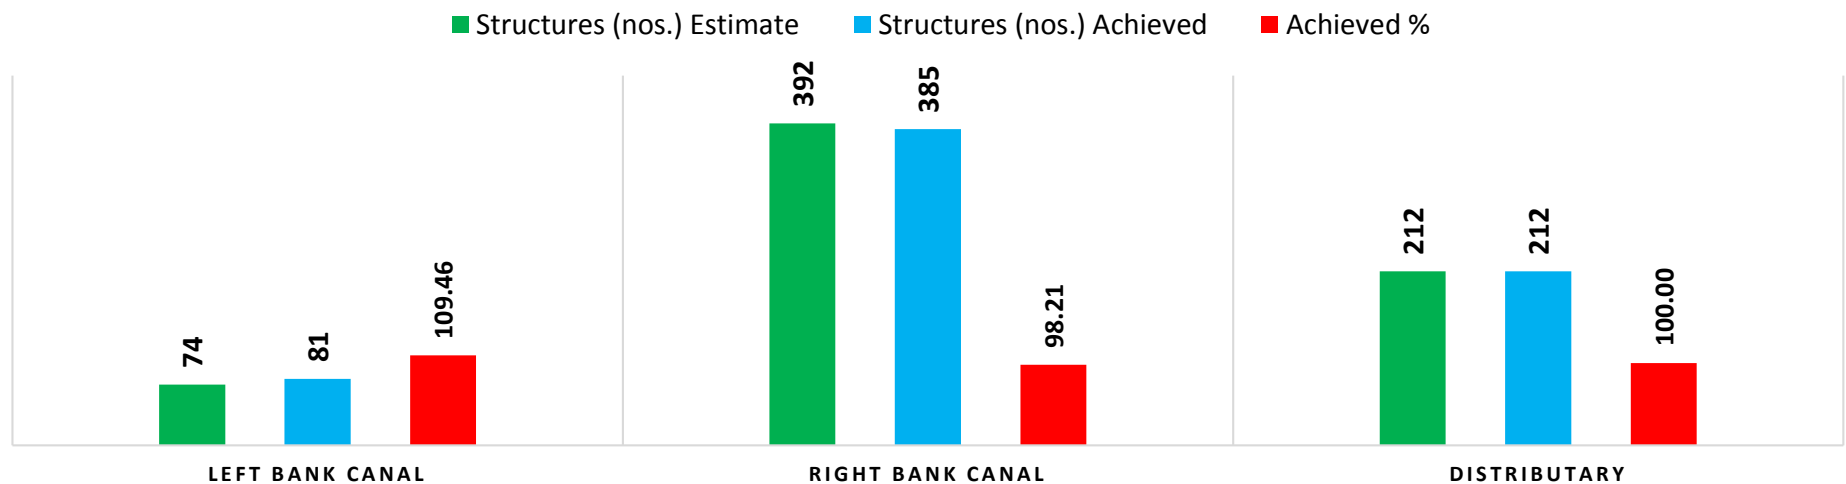

Gondi Main works: Financial Progress as of 31 December 2019

S.No	Item of work	Lining (crore)		Achieved	Structures (crore)		Achieved
		Estimate	Achieved	%	Estimate	Achieved	%
1	Left Bank Canal	8.9	8.77	98.54	1.76	1.76	100.00
2	Right Bank Canal	82.71	82.39	99.61	27.97	26.99	96.50
3	Distributary	5.42	5.33	98.34	2.18	2.18	100.00

Financial Progress: Lining

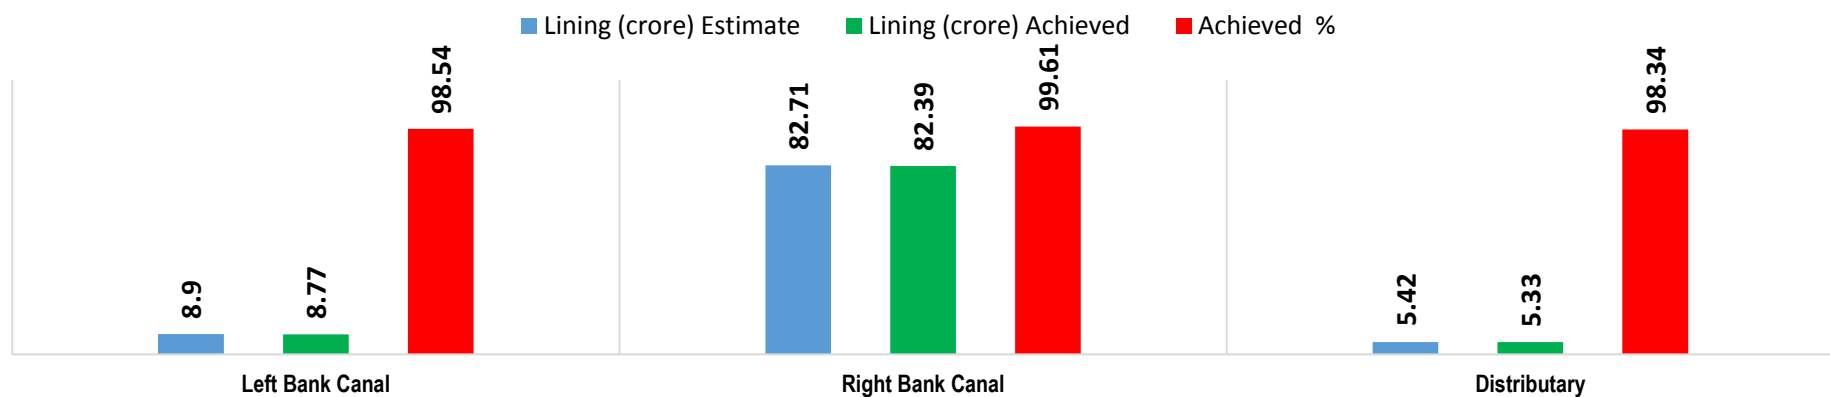

Financial Progress: Structures

