


Physical Progress as on 30 November 2017							
S.No	Item of work	Lining (Km)		Achievement	Structures (Nos.)		Achievement
		Estimate	Achievement	%	Estimate	Achievement	%
1	Left Bank Canal	14.74	14.20	96	74	74	100
2	Right Bank Canal	74.24	50.12	68	392	321	82
3	Distributary	26.1	26.10	100	212	212	100

PHYSICAL PROGRESS:LINING



PHYSICAL PROGRESS:STRUCTURES

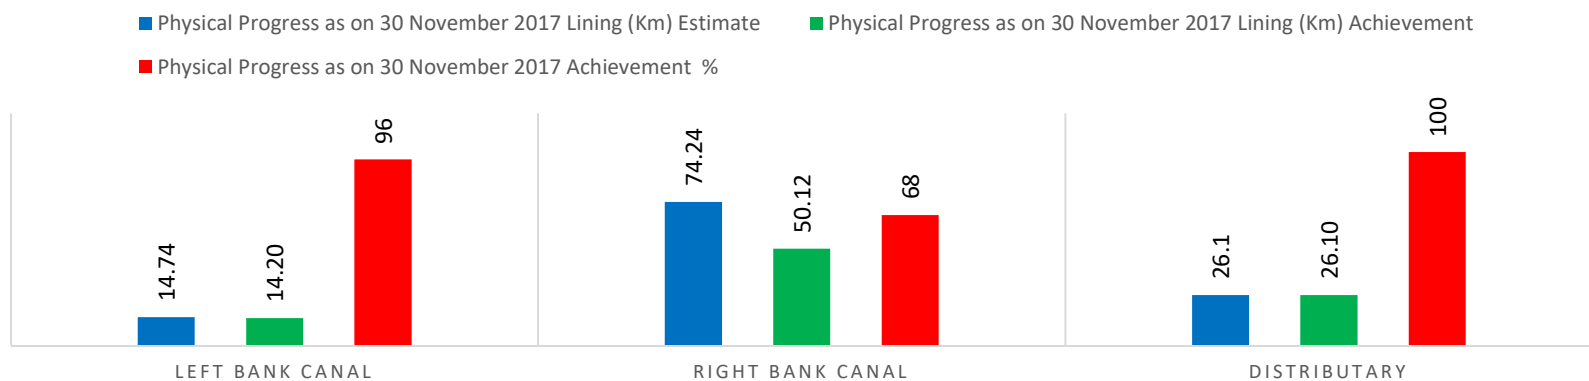
