


Physical Progress as on 30 September 2017							
S.No	Item of work	Lining (Km)		Achievment	Structures (Nos.)		Achievment
		Estimate	Achievment	%	Estimate	Achievment	%
1	Left Bank Canal	14.74	14.20	96.34	74	74	100.00
2	Right Bank Canal	74.24	42.88	57.76	392	286	72.96
3	Distributary	26.1	24.30	93.10	212	212	100.00

PHYSICAL PROGRESS:LINING



PHYSICAL PROGRESS:STRUCTURES

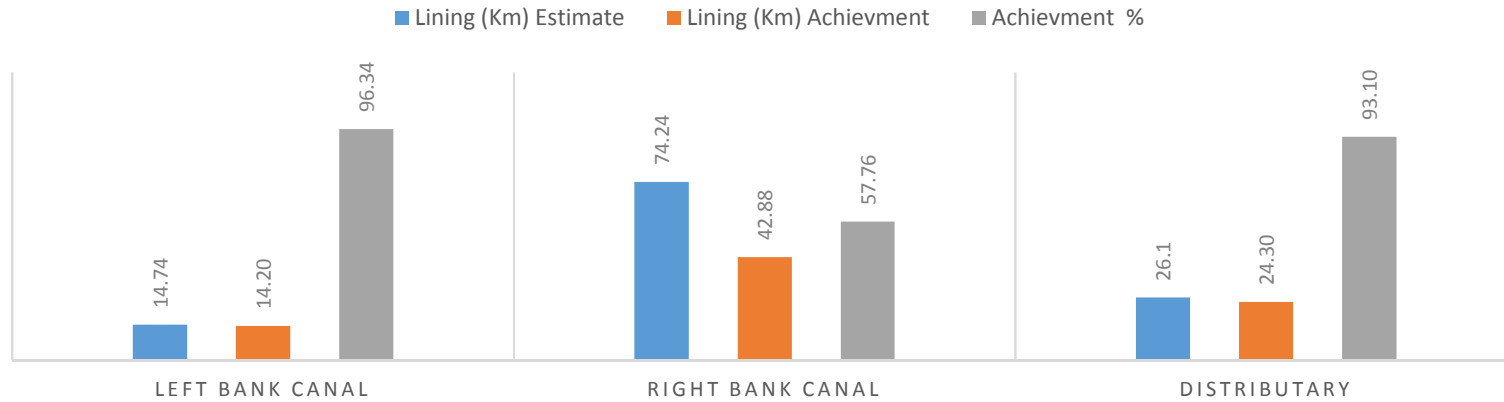
