



Vijayanagar main channel works: Physical Progress upto 30.09.2021

S.No	Item of work	Lining (km)		Achieved	Structures (nos.)		Achieved
		Estimate	Achieved	%	Estimate	Achieved	%
RBC							
1	Raya	27.74	4.27	15.37	100	18	18.00
2	Basavanna	16.50	6.85	41.48	71	26	36.62
3	Bella	5.50	3.20	58.24	52	31	59.62
4	Kalaghatta	7.02	4.07	57.91	49	19	38.78
5	Ramsagara	15.50	2.1	13.55	57	11	19.30
6	Kampli	23.55			124		
7	Belagodahalla	11.22			82		
8	Deshnuru	9.03	5.412	59.93	30	14	46.67
9	Siruguppa	10.85	9.289	85.61	16	13	81.25
LBC							
10	Huligi	10.69	5.165	48.32	104	16	15.38
11	Shivapura	6.54	3.558	54.40	58	10	17.24
12	Anegundi	19.44	4.17	21.45	148	25	16.89
13	Upper Gangavathi	9.00	0.99	11.00	66	3	4.55
14	Lower Gangavathi	9.54	1.087	11.39	62	5	8.06
15	Bichal	14.50	3.25	22.41	23	6	26.09
	Total	196.62	53.40	27.16	1042	197	18.91

Physical Progress: Lining

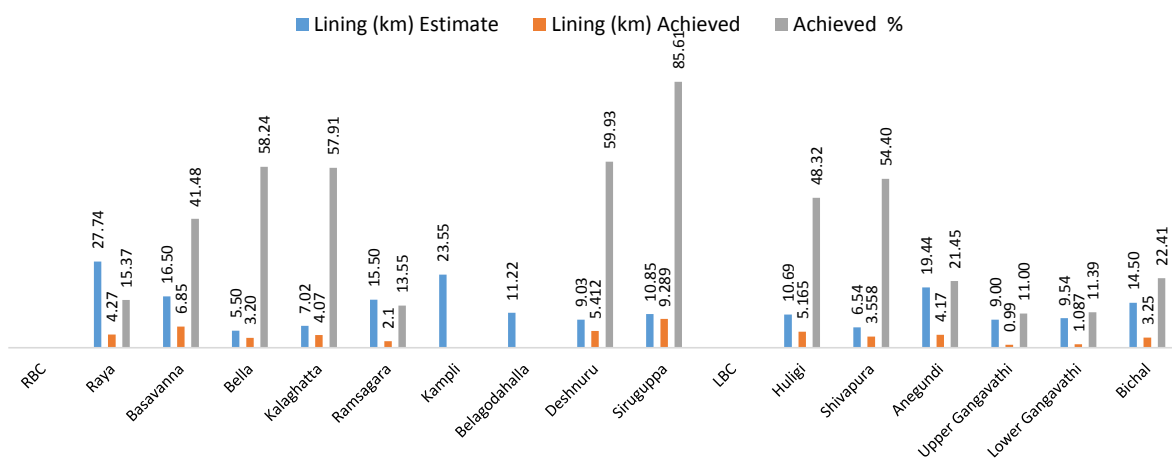


Physical Progress: Structures

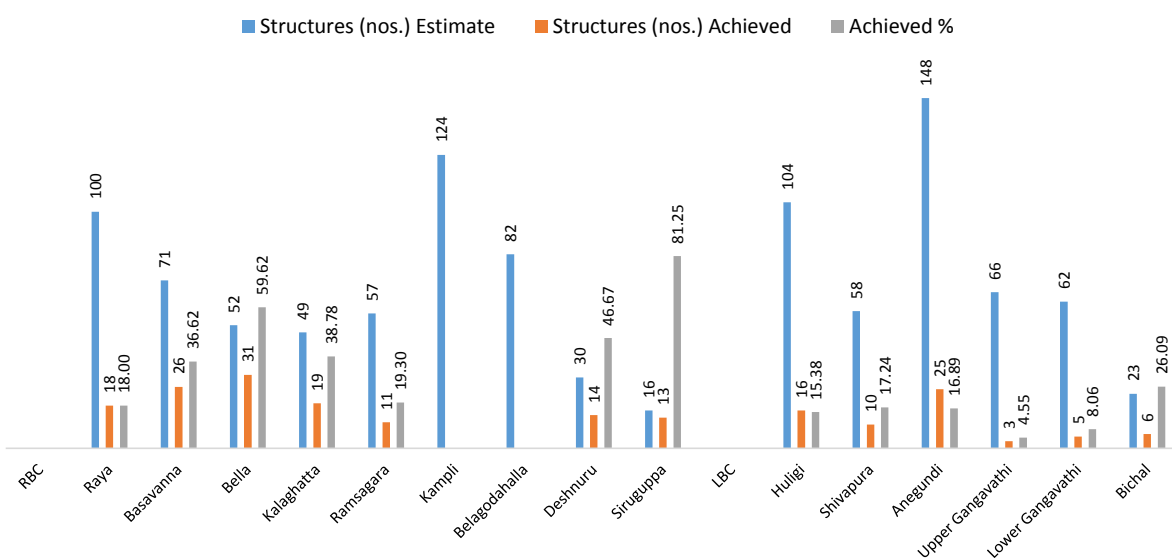

Vijayanagar main channel works: Financial Progress as of 30.09.2021							
S.No	Item of work	Lining (Crores)		Achieved	Structures (Crores)		Achieved
		Estimate	Achieved	%	Estimate	Achieved	%
RBC							
1	Raya	52.94	11.41	21.55	3.96	2.66	67.26
2	Basavanna	22.10	15.72	71.15	4.65	2.54	54.61
3	Bella	11.33	6.50	57.37	4.23	2.52	59.57
4	Kalaghatta	12.45	6.49	52.11	3.21	1.24	38.75
5	Ramsagara	30.17	3.83	12.69		1.28	
6	Kampli	29.92	0.00	0.00			
7	Belagodahalla	12.97	0.00	0.00			
8	Deshnuru	15.66	9.39	59.96	2.18	1.02	46.79
9	Siruguppa	16.04	13.54	84.41	1.61	1.59	
LBC							
10	Huligi	14.28	5.88	41.18	3.96	1.17	29.46
11	Shivapura	10.46	4.86	46.46	1.68	0.31	18.57
12	Anegundi	38.91	8.53	21.92	1.88	1.17	62.34
13	Upper Gangavathi	32.81	3.61	11.00	1.02	0.92	89.85
14	Lower Gangavathi	30.99	3.53	11.39	4.83	0.81	16.74
15	Bichal	17.56	4.53	25.80		1.00	
	Total	348.59	97.82	28.06	33.21	18.23	54.88

Financial Progress: Lining

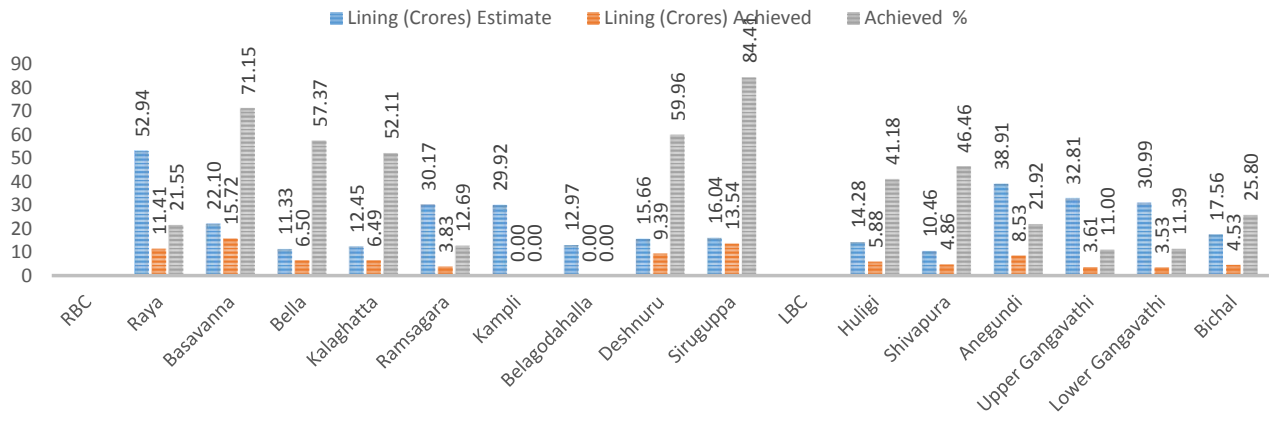

Financial progress: Structures

