


Physical Progress as on 31 August 2017							
S.No		Lining (Km)		Achievment	Structures (Nos.)		Achievment
		Estimate	Achievment	%	Estimate	Achievment	%
1	Left Bank Canal	14.735	14.20	96.37	74	74	100.00
2	Right Bank Canal	74.239	41.51	55.91	392	248	63.27
3	Distributary	26.64	24.30	91.22	212	212	100.00

PHYSICAL PROGRESS:LINING



PHYSICAL PROGRESS:STRUCTURES

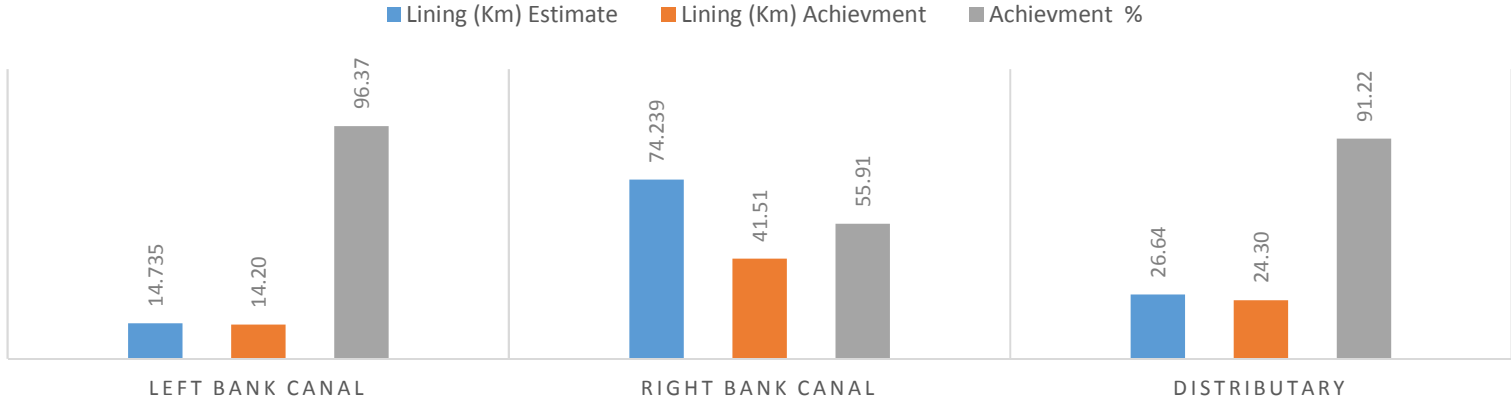
