



CAD Physical Progress as of 31 January 2018

S.No	Name of the WUCS	Lining (km)		Achievement	Structures (nos.)		Achievement
		Estimate	Achievement	%	Estimate	Achievement	%
1	Doddagoppenahalli	10.77	4.70	44	147	38	26
2	Baranduru	27.32	25.23	92	376	330	88
3	Seegebagi	11.37	10.27	90	169	90	53
4	Baballi	23.44	22.90	98	201	193	96
5	Kagekodamagge	11.36	11.07	97	114	105	92
6	Talrikatte	11.40	10.83	95	128	89	70
7	Nagatibelagalu	15.16	11.99	79	231	115	50
8	Dasarakallahalli	18.38	15.65	85	208	113	54
9	Koppadoddakere	16.11	12.25	76	188	74	39
10	Holehonnuru	11.25	8.85	79	107	66	62
11	Mudalavittalapura	9.20	3.50	38	71	15	21

PHYSICAL PROGRESS: LINING

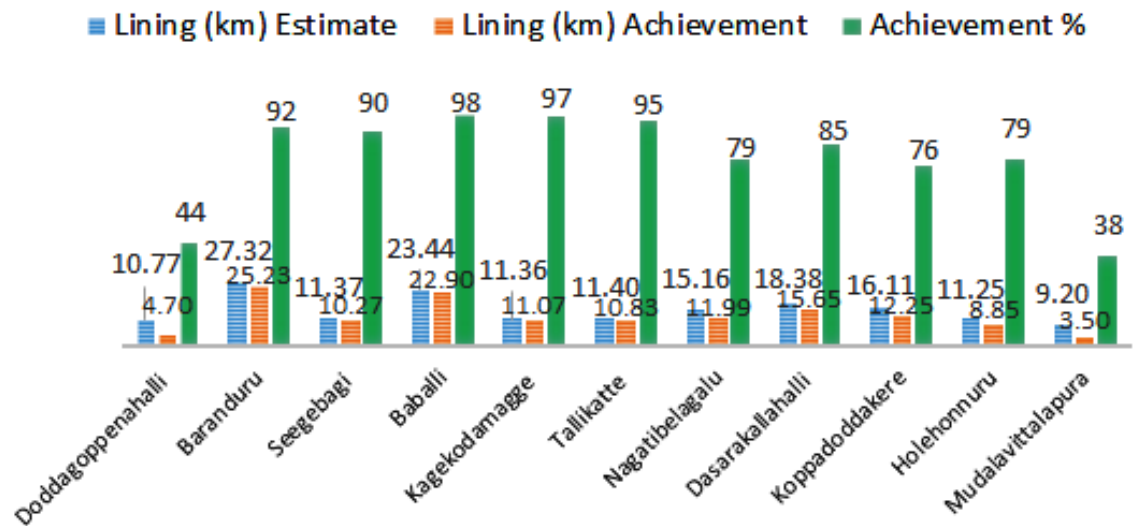

PHYSICAL PROGRESS: STRUCTURES

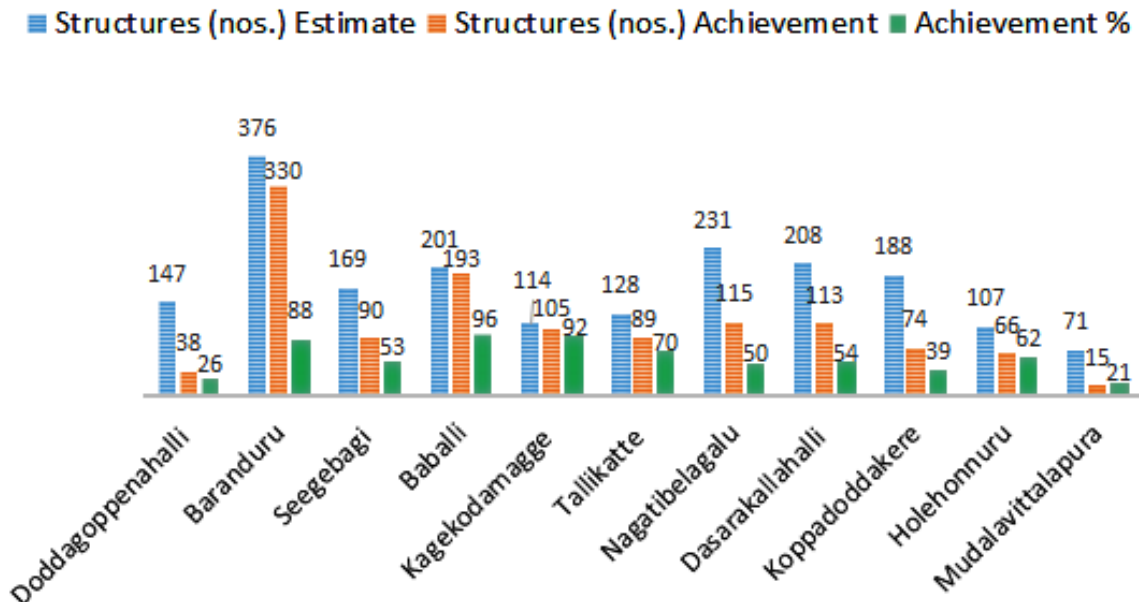

**GONDI WUCS-CAD Package Works:
Financial Progress as of 31 January 2018**

S. No	Name of the WUCS	Command Area (ha)	No of CAD Package	Estimated amount (INR Lakhs)	Agreement amount (INR lakhs)	Financial	Total expenditure (INR lakhs)
1	Doddagoppenahalli	212.00	8	145.45	144.52	14.45	39.72
2	Baranduru	614.00	20	359.46	357.93	35.79	277.05
3	Seegebagi	368.50	9	144.00	142.74	14.27	71.72
4	Baballi	593.00	20	299.73	298.13	29.81	172.82
5	Kagekodamagge	322.90	9	163.50	162.73	16.27	134.3
6	Talrikatte	372.80	10	183.00	180.86	18.08	86.07
7	Nagatibelagalu	334.90	8	145.45	143.62	14.36	74.20
8	Dasarakallhalli	506.60	13	252.00	249.49	24.94	123.79
9	Koppadoddakere	598.47	12	238.00	235.75	23.57	102.87
10	Holehonnuru	340.93	8	148.00	146.09	14.60	33.35
11	Mudalavitalapura	318.34	7	120.00	1	11.85	29.95
	Total	4582.44	124	2198.59	2062.86	217.99	1145.84

Financial progress

