


CAD Physical Progress as of 31 March 2018

| S.No | Name of the WUCS | Lining (km) | | Achievement | Structures (nos.) | | Achievement |
|------|-------------------|-------------|-------------|-------------|-------------------|-------------|-------------|
| | | Estimate | Achievement | % | Estimate | Achievement | % |
| 1 | Doddagoppenahalli | 10.77 | 6.20 | 58 | 147 | 38 | 26 |
| 2 | Baranduru | 27.32 | 25.67 | 94 | 376 | 330 | 88 |
| 3 | Seegebagi | 11.37 | 10.27 | 90 | 169 | 90 | 53 |
| 4 | Baballi | 23.44 | 23.44 | 100 | 201 | 201 | 100 |
| 5 | Kagekodamagge | 11.36 | 11.36 | 100 | 114 | 112 | 98 |
| 6 | Tallikatte | 11.40 | 11.30 | 99 | 128 | 95 | 74 |
| 7 | Nagatibelagalu | 15.16 | 12.48 | 82 | 231 | 115 | 50 |
| 8 | Dasarakallahalli | 18.38 | 16.00 | 87 | 208 | 127 | 61 |
| 9 | Koppadoddakere | 16.11 | 12.65 | 79 | 188 | 89 | 47 |
| 10 | Holehonnuru | 11.25 | 8.85 | 79 | 107 | 66 | 62 |
| 11 | Mudalavittalapura | 9.20 | 5.30 | 58 | 71 | 24 | 34 |

PHYSICAL PROGRESS: LINING

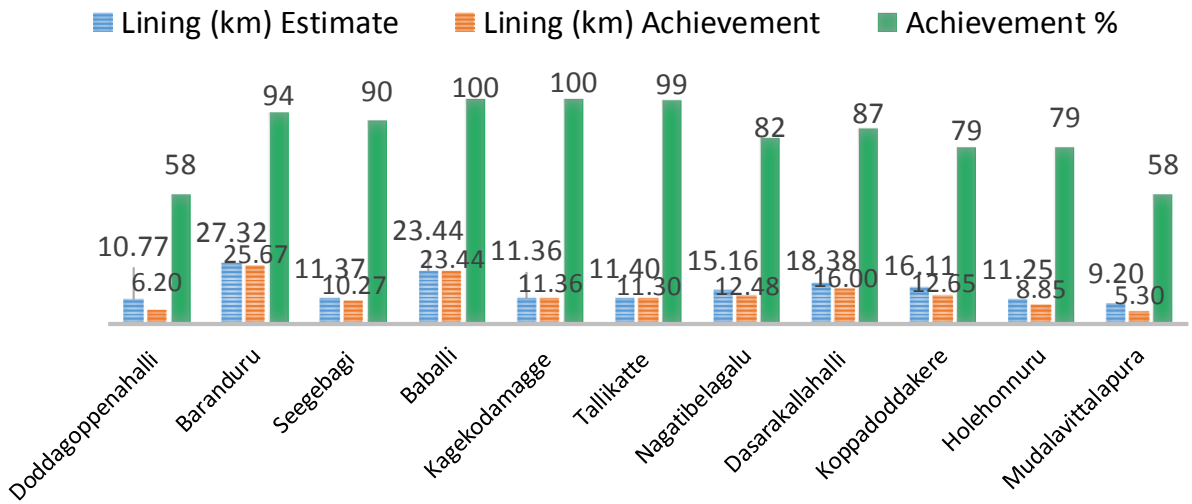

PHYSICAL PROGRESS: STRUCTURES

