


### CAD Physical Progress as of 30 May 2018

S.No	Name of the WUCS	Lining (km)		Achievement	Structures (nos.)		Achievement
		Estimate	Achievement	%	Estimate	Achievement	%
1	Doddagoppenahalli	10.77	6.20	58	147	38	26
2	Baranduru	27.32	25.67	94	376	330	88
3	Seegebagi	11.37	10.82	95	169	90	53
4	Baballi	23.44	23.44	100	201	201	100
5	Kagekodamagge	11.36	11.36	100	114	112	98
6	Tallikatte	11.40	11.30	99	128	95	74
7	Nagatibelagalu	15.16	12.48	82	231	115	50
8	Dasarakallahalli	18.38	16.00	87	208	127	61
9	Koppadoddakere	16.11	12.65	79	188	89	47
10	Holehonnuru	11.25	8.85	79	107	66	62
11	Mudalavittalapura	9.20	5.30	58	71	24	34

### PHYSICAL PROGRESS: LINING

■ Lining (km) Estimate    
 ■ Lining (km) Achievement    
 ■ Achievement %

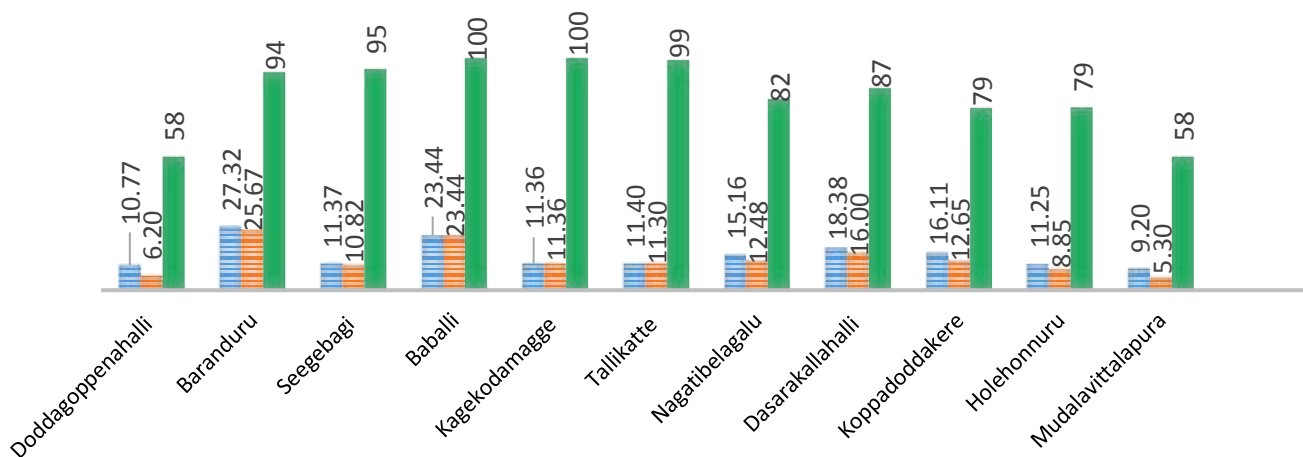

### PHYSICAL PROGRESS: STRUCTURES

■ Structures (nos.) Estimate    
 ■ Structures (nos.) Achievement    
 ■ Achievement %

