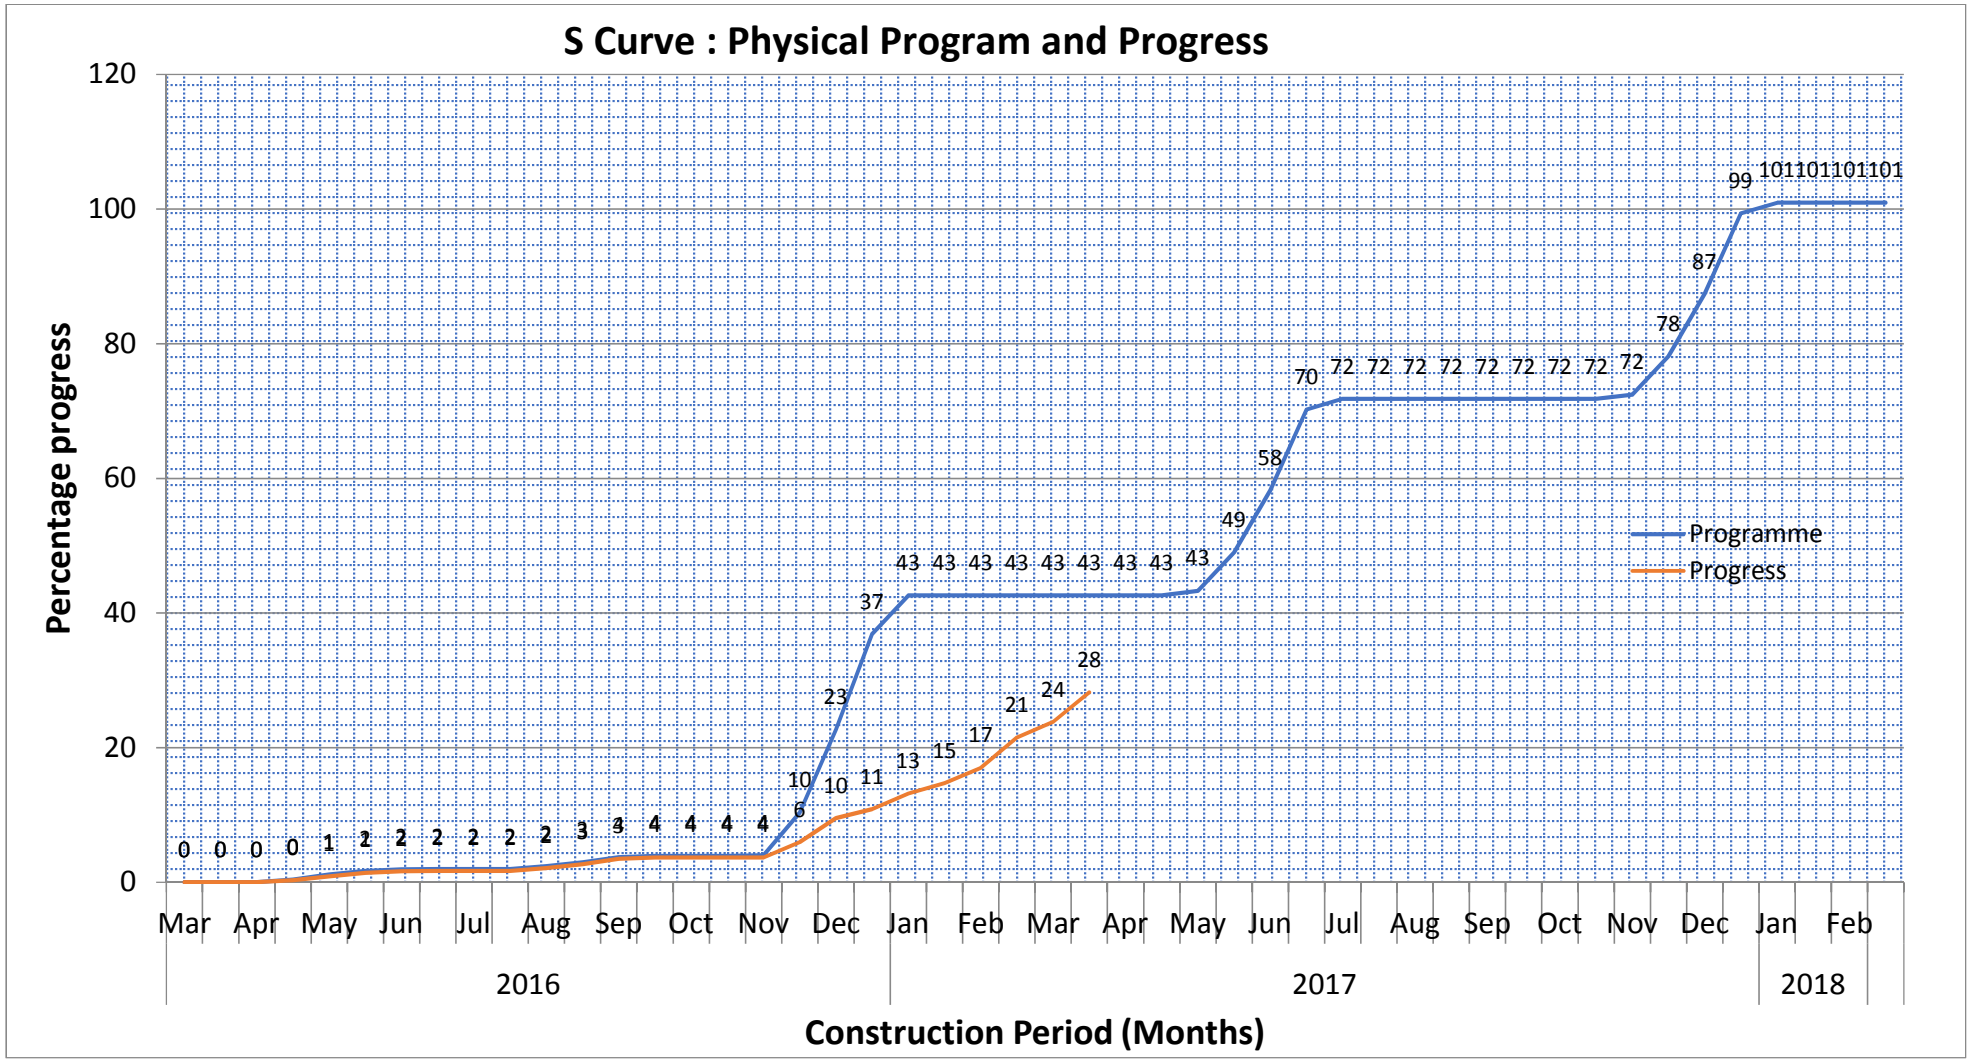
S Curve : Physical Program and Progress
Percentage progress
120
100
80
60
40
20
0
Programme
Progress
Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb
2016
2017
2018
Construction Period (Months)

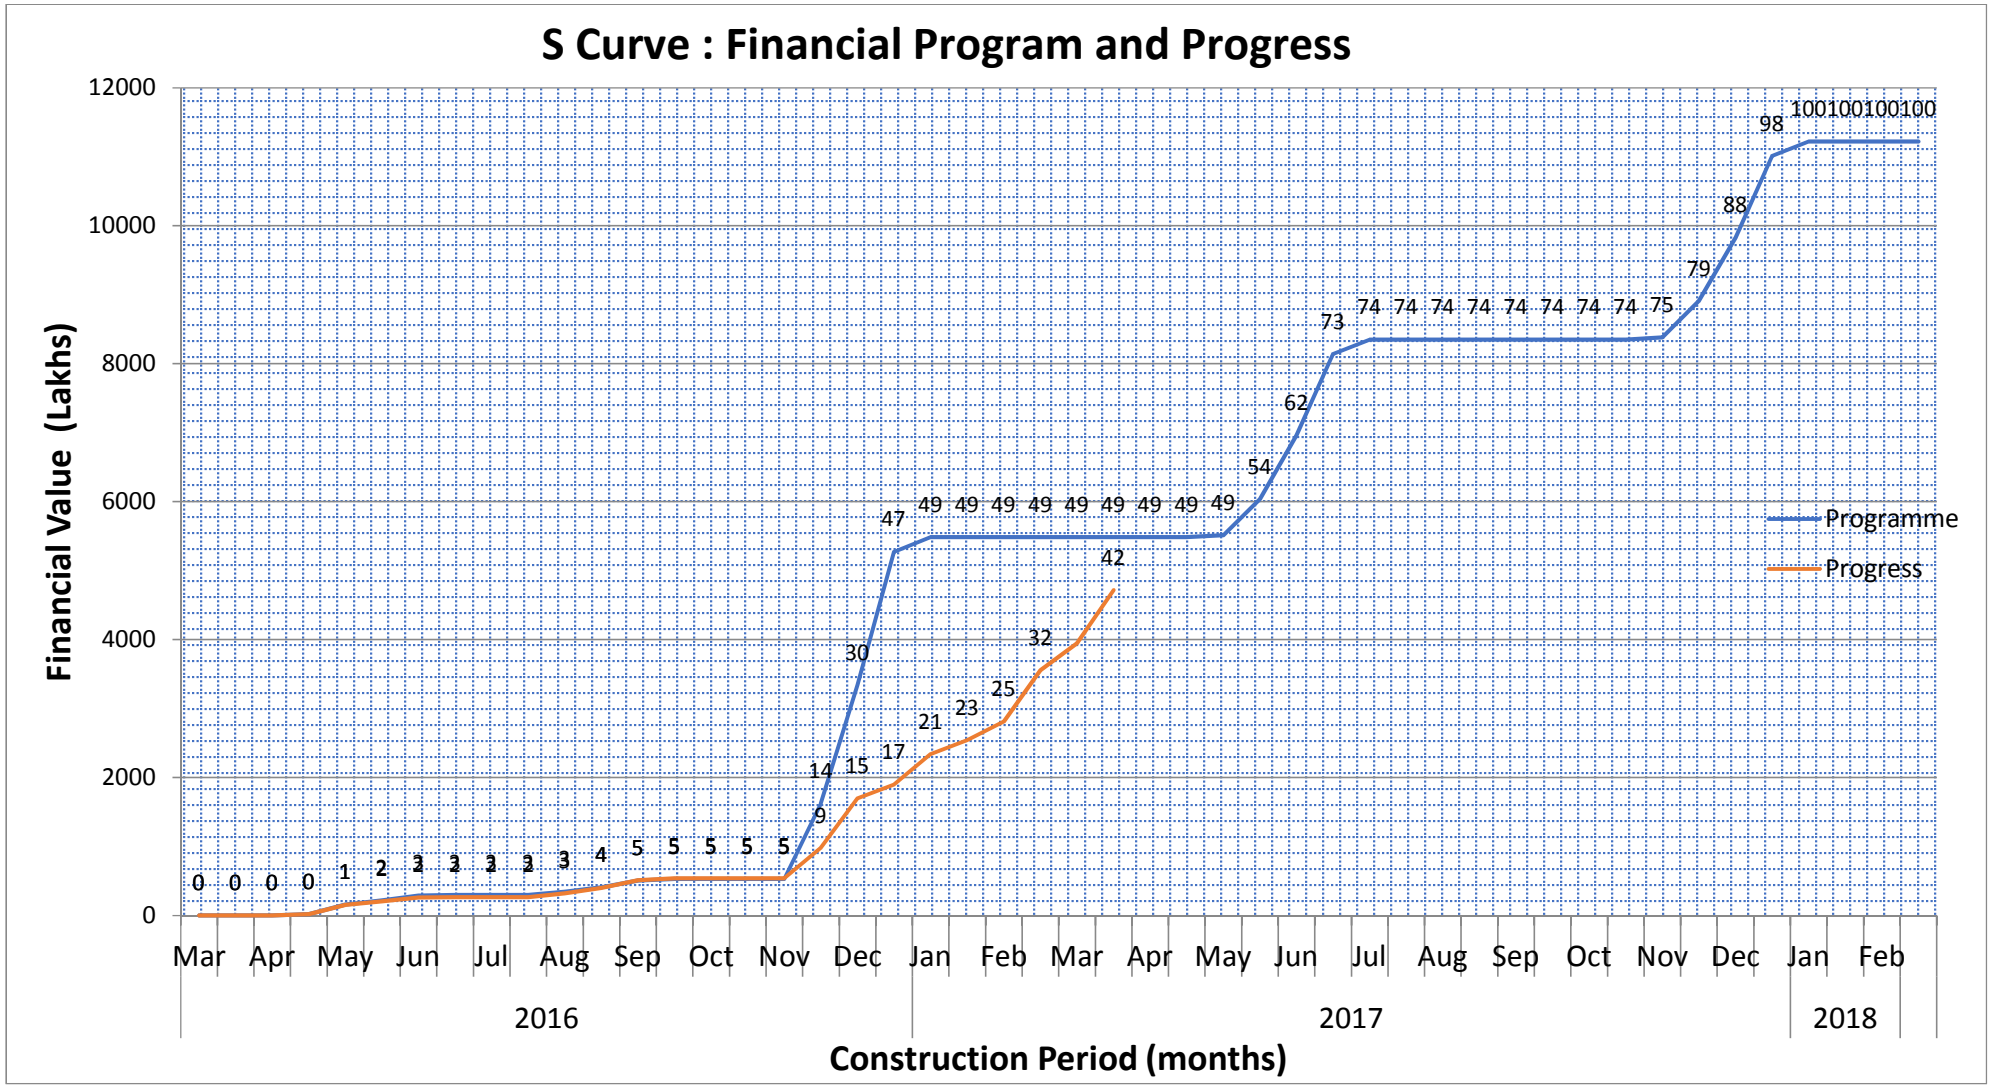
S Curve : Financial Program and Progress
Financial Value (Lakhs)
12000
10000
8000
6000
4000
2000
0
Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb
2016
2017
2018
Construction Period (months)
Programme
Progress
0 0 0 0 1 2 2 2 2 2 3 4 5 5 5 5 5
9 14 15 17 21 23 25 32 42
30 47 49 49 49 49 49 49 49 49 49 54 62 73 74 74 74 74 74 74 74 74 75 79 88 98 100100100100
